ID		Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish
1	✓		Preconstruction Conference	1 day	Fri 12/20/19	Fri 12/20/19	Fri 12/20/19	Fri 12/20/19
2			NTP	0 days	Fri 12/20/19	Fri 12/20/19	NA	NA
3	✓		Mobilization	1 day	Mon 1/6/20	Mon 1/6/20	Mon 1/6/20	Mon 1/6/20
4			**Phase I - East Allen Rd to Miller**	**152 days**	**Tue 12/17/19**	**Wed 7/15/20**	**Tue 12/17/19**	**NA**
5	✓		Wide Area conference	0 days	Tue 12/17/19	Tue 12/17/19	Tue 12/17/19	Tue 12/17/19
6			Traffic control	2 days	Mon 1/6/20	Wed 1/8/20	Mon 1/6/20	NA
7	✓		Install Fence	2 days	Wed 1/8/20	Fri 1/10/20	Wed 1/8/20	Fri 1/10/20
8	✓		Milling Surface	2 days	Mon 1/13/20	Tue 1/14/20	Mon 1/13/20	Tue 1/14/20
9	✓		Remove Concrete	8 days	Wed 1/15/20	Fri 1/24/20	Wed 1/15/20	Fri 1/24/20
10	✓		Remove Elect Signals	0 days	Fri 1/10/20	Fri 1/10/20	Fri 1/10/20	Fri 1/10/20
11			**WaterLine**	**32 days**	**Mon 1/27/20**	**Tue 3/10/20**	**NA**	**NA**
12			Install Water Line, 975 LF allen to miller	13 days	Mon 1/27/20	Wed 2/12/20	NA	NA
13			Install Water Line Wall street 147 LF	2 days	Thu 2/13/20	Fri 2/14/20	NA	NA
14			Install 10" Waterline Orchard Street 165 LF	2 days	Mon 2/17/20	Tue 2/18/20	NA	NA
15			Chlorinate and Test Waterline	2 days	Wed 2/19/20	Thu 2/20/20	NA	NA
16			Bac- Test Waterline	1 day	Fri 2/21/20	Fri 2/21/20	NA	NA
17			Tie in New waterline to Existing	1 day	Mon 2/24/20	Mon 2/24/20	NA	NA
18			Cut over New Water line Services, 41 services	11 days	Tue 2/25/20	Tue 3/10/20	NA	NA
19			**StormDrain**	**39 days**	**Thu 2/13/20**	**Tue 4/7/20**	**NA**	**NA**
20			Install New Storm Drain, 36" HDPE, 504.39 LF	9 days	Thu 2/13/20	Tue 2/25/20	NA	NA
21			Install New Storm Drain, 30" HDPE, 302.2 LF	5 days	Wed 2/26/20	Tue 3/3/20	NA	NA
22			Install New Storm Drain, 24" HDPE, 302.85 LF	5 days	Wed 3/4/20	Tue 3/10/20	NA	NA
23			Install New Storm Drain, 18" HDPE, 353.92 LF	5 days	Wed 3/11/20	Tue 3/17/20	NA	NA
24			Build Manholes, 6 each 4' Dia, 4 each 6' Dia, 1 each 7' Dia, 9 each 8' Dia	14 days	Wed 2/26/20	Mon 3/16/20	NA	NA
25			Build New Inlets, 11 each Curb inlets, 4 each surface, 20 each double curb	20 days	Wed 3/11/20	Tue 4/7/20	NA	NA
26			Build New LID's	15 days	Wed 2/26/20	Tue 3/17/20	NA	NA
27			New Curb and Gutter	25 days	Fri 3/20/20	Thu 4/23/20	NA	NA
28			Build New SW Scuppers	10 days	Fri 4/24/20	Thu 5/7/20	NA	NA
29			Subgrade prep for pavers	7 days	Fri 4/24/20	Mon 5/4/20	NA	NA
30			New Sidewalk	15 days	Fri 5/8/20	Thu 5/28/20	NA	NA
31			Build new planters	10 days	Tue 5/19/20	Mon 6/1/20	NA	NA
32			Build new Concrete ret Walls	12 days	Tue 6/2/20	Wed 6/17/20	NA	NA
33			Remove Concrete SW from Building	5 days	Thu 6/18/20	Wed 6/24/20	NA	NA
34			New SW building	15 days	Thu 6/25/20	Wed 7/15/20	NA	NA
35			Install New Pavers	24 days	Tue 5/19/20	Fri 6/19/20	NA	NA
36			Build New Concrete collars, MH, FH, Valves	12 days	Tue 3/17/20	Wed 4/1/20	NA	NA
37			Install New Irrigation Conduit and wiring	15 days	Fri 4/24/20	Thu 5/14/20	NA	NA
38			Install new Electrical Conduit and wiring	10 days	Fri 4/24/20	Thu 5/7/20	NA	NA
39			Install Sleeves (Elect & Irrigation)	5 days	Fri 4/24/20	Thu 4/30/20	NA	NA
40			Subgrade Prep	5 days	Fri 5/15/20	Thu 5/21/20	NA	NA
41			Base course	5 days	Fri 5/22/20	Thu 5/28/20	NA	NA
42			Apshalt Pave	5 days	Fri 5/29/20	Thu 6/4/20	NA	NA
43			Stripe	5 days	Fri 6/5/20	Thu 6/11/20	NA	NA
44			Install new Lights & Appurtaences	10 days	Fri 5/8/20	Thu 5/21/20	NA	NA
45			EOPhase I	0 days	Wed 7/15/20	Wed 7/15/20	NA	NA
46			**Phase II - West Allen Rd to Auburn**	**95 days?**	**Wed 7/15/20**	**Tue 11/24/20**	**NA**	**NA**
47			Wide Area conference	1 day	Thu 7/16/20	Thu 7/16/20	NA	NA
48			Traffic control	2 days	Fri 7/17/20	Mon 7/20/20	NA	NA

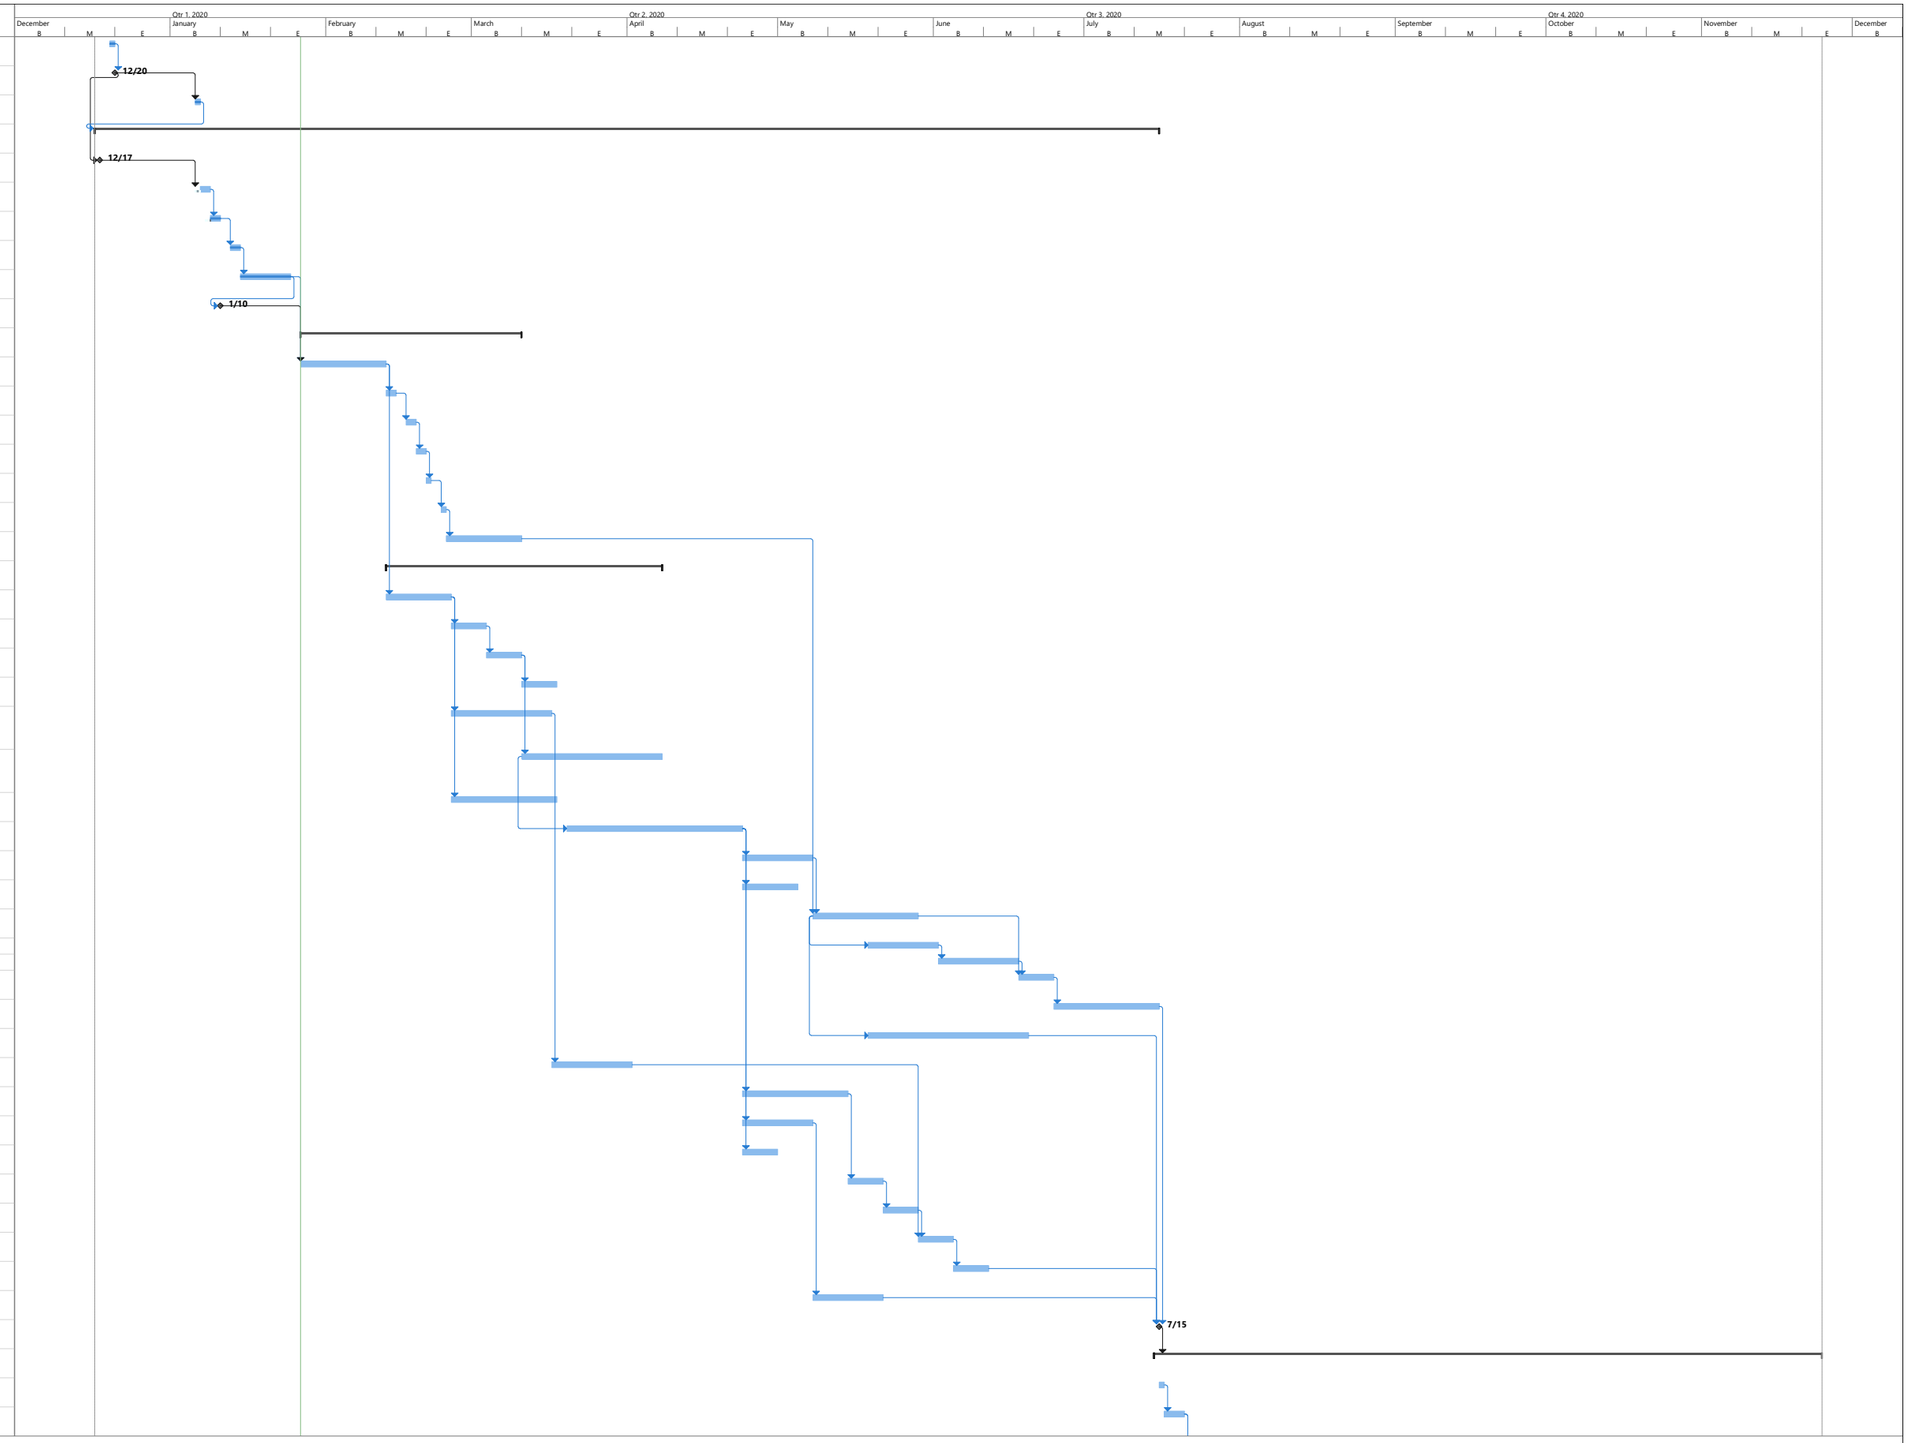

Project: 102402020 Schedule Fa
Date: Mon 1/27/20

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

ID		Task Mode	Task Name	Duration	Start	Finish	Actual Start	Actual Finish
49			Install Fence	2 days	Tue 7/21/20	Wed 7/22/20	NA	NA
50			Milling Surface	2 days	Thu 7/23/20	Fri 7/24/20	NA	NA
51			Remove Concrete	7 days	Mon 7/27/20	Tue 8/4/20	NA	NA
52			Remove Electrical Signals	2 days	Tue 7/21/20	Wed 7/22/20	NA	NA
53			Waterline				NA	NA
54			**Install Water Line, 1154.55 LF Allen to Auburn**	**17 days**	**Mon 7/27/20**	**Tue 8/18/20**	**NA**	**NA**
55			Install Water Line Allen street 163 LF 8" WL	2 days	Mon 7/27/20	Tue 7/28/20	NA	NA
56			Install 8" Waterline Behrend Street 103.81 LF WL South, 22' North	2 days	Mon 7/27/20	Tue 7/28/20	NA	NA
57			Install 8" Waterline Locke Street 105.05 LF WL North	2 days	Mon 7/27/20	Tue 7/28/20	NA	NA
58			Chlorinate and Test Waterline	2 days	Wed 7/29/20	Thu 7/30/20	NA	NA
59			Bac- Test Waterline	1 day	Fri 7/31/20	Fri 7/31/20	NA	NA
60			Tie in New waterline to Existing	1 day	Mon 8/3/20	Mon 8/3/20	NA	NA
61			Cut over New Water line Services, 41 services	11 days	Tue 8/4/20	Tue 8/18/20	NA	NA
62			**Stormdrain**	**46 days**	**Mon 7/27/20**	**Mon 9/28/20**	**NA**	**NA**
63			Install New Storm Drain Allen 36" HDPE, 359.38 LF	4 days	Mon 7/27/20	Thu 7/30/20	NA	NA
64			Install New Storm Drain, 24" HDPE, 100.2 LF Main @ Allen	2 days	Fri 7/31/20	Mon 8/3/20	NA	NA
65			Install New Storm Drain, 36" HDPE, 338.81 LF BEHREND	5 days	Tue 8/4/20	Mon 8/10/20	NA	NA
66			Install New Storm Drain, 18" HDPE, 266.32 LF Main st at BEHREND	5 days	Tue 8/11/20	Mon 8/17/20	NA	NA
67			Install New Storm Drain, 24" HDPE, 83.69 LF, 224.62 LF 18" HDPE Main st @Locke	5 days	Tue 8/18/20	Mon 8/24/20	NA	NA
68			Install New Storm Drain, 36" HDPE, 106.40 LF Locke st, 24" HDPE, 74.20 LF Locke, 18" HDPE 30 LF at Main	4 days	Tue 8/25/20	Fri 8/28/20	NA	NA
69			Install New Storm Drain, 18" HDPE, 72.02 LF Main st @Auburn	1 day	Mon 8/31/20	Mon 8/31/20	NA	NA
70			Install New Storm Drain, 48" HDPE, 173.00 LF Auburn, 24" HDPE, 74.28 LF Auburn, 18" HDPE 47.44 LF @ Main	4 days	Tue 9/1/20	Fri 9/4/20	NA	NA
71			Build Manholes, 6 each 4' Dia, 4 each 6' Dia, 1 each 7' Dia, 9 each 8' Dia	14 days	Fri 7/31/20	Wed 8/19/20	NA	NA
72			Build New Inlets, 11 each Curb inlets, 4 each surface, 20 each double curb	20 days	Tue 9/1/20	Mon 9/28/20	NA	NA
73			Build New LID's Allen	6 days	Fri 7/31/20	Fri 8/7/20	NA	NA
74			New Curb and Gutter	15 days	Thu 9/10/20	Wed 9/30/20	NA	NA
75			Build New SW Scuppers	7 days	Tue 9/15/20	Wed 9/23/20	NA	NA
76			Subgrade prep for pavers	7 days	Thu 10/1/20	Fri 10/9/20	NA	NA
77			New Sidewalk	15 days	Thu 9/24/20	Wed 10/14/20	NA	NA
78			Build new planters	10 days	Mon 10/5/20	Fri 10/16/20	NA	NA
79			Build new Concrete ret Walls	10 days	Mon 10/19/20	Fri 10/30/20	NA	NA
80			Remove Concrete SW from Building	5 days	Mon 11/2/20	Fri 11/6/20	NA	NA
81			New SW building	15 days	Wed 11/4/20	Tue 11/24/20	NA	NA
82			Install New Pavers	24 days	Thu 10/1/20	Tue 11/3/20	NA	NA
83			Build New Concrete collars, MH, FH, Valves	10 days	Thu 8/20/20	Wed 9/2/20	NA	NA
84			Install New Irrigation Conduit and wiring	15 days	Thu 10/1/20	Wed 10/21/20	NA	NA
85			Install new Electrical Conduit and wiring	10 days	Thu 10/1/20	Wed 10/14/20	NA	NA
86			Install Sleeves (Elect & Irrigation)	4 days	Thu 10/1/20	Tue 10/6/20	NA	NA
87			Subgrade Prep	5 days	Thu 10/22/20	Wed 10/28/20	NA	NA
88			Base course	5 days	Thu 10/29/20	Wed 11/4/20	NA	NA
89			Apshalt Pave	5 days	Thu 11/5/20	Wed 11/11/20	NA	NA
90			Stripe	5 days	Thu 11/12/20	Wed 11/18/20	NA	NA
91			Install new Lights & Appurtenances	10 days	Thu 10/15/20	Wed 10/28/20	NA	NA
92			EOPhase II	0 days	Mon 11/2/20	Mon 11/2/20	NA	NA

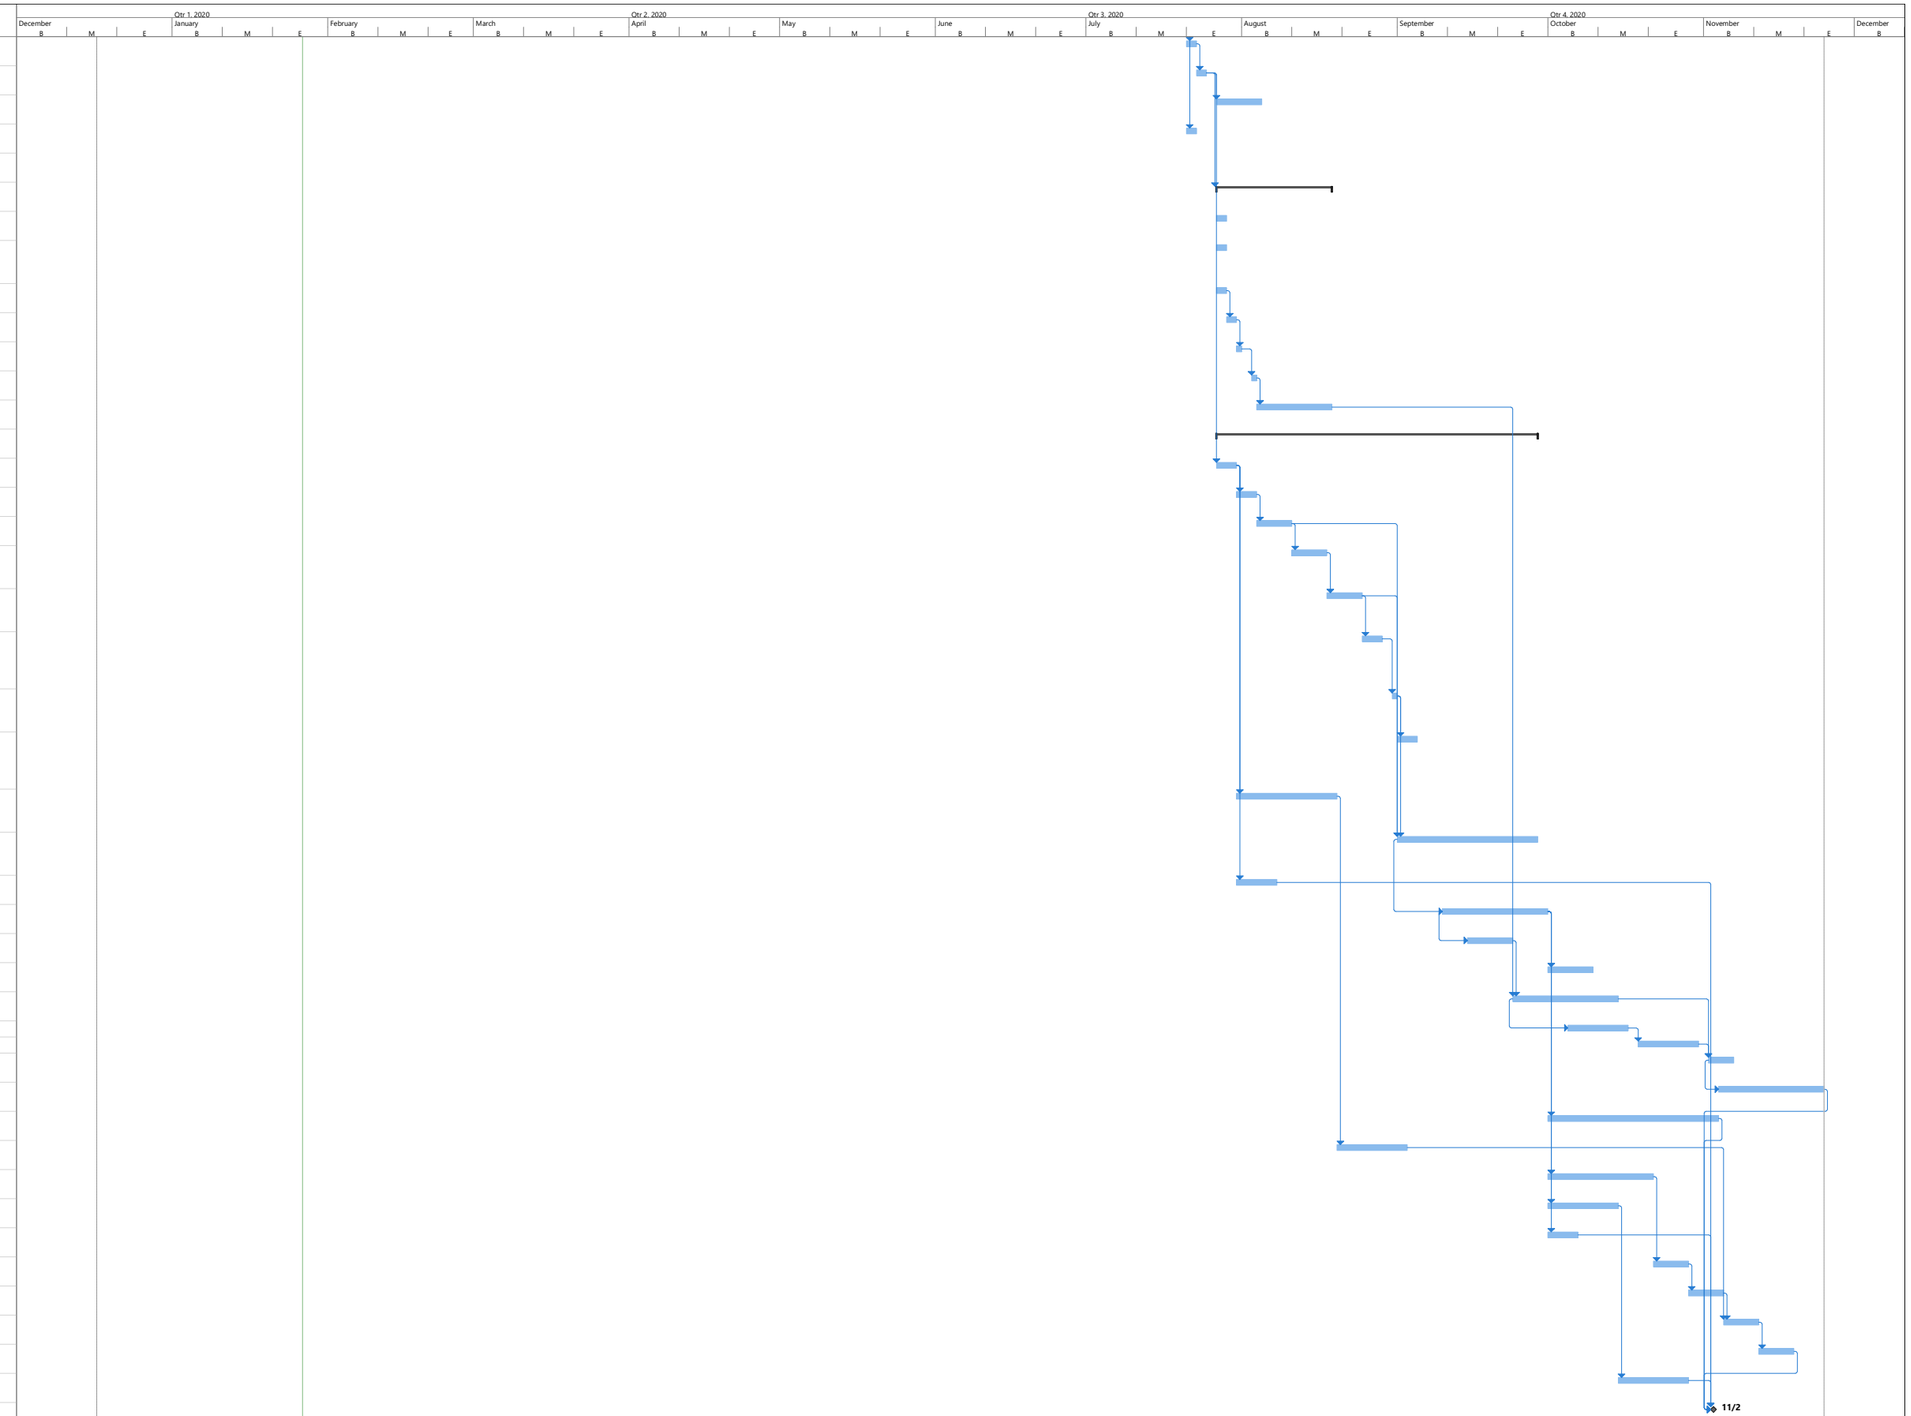

Project: 102402020 Schedule Fa
Date: Mon 1/27/20

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
